

**Staff Report on Howard W. Peak Greenway Trails Progress
(Brandon Ross, Parks and Recreation) 8/25/20**

Salado Creek Greenway (Projects listed North to South)

- Salado (Loop 1604 to Eisenhower Park) – 3 miles north of Loop 1604 Trailhead adjacent to Salado Creek completed and opened to the public in June. Eisenhower Trailhead and portion between quarry and Camp Bullis to be opened December 2020.
- John James Park to Jack White Park (Ft. Sam Houston Connection – 3.9 miles) – Working with Joint Base San Antonio (JBSA) to demolish old horse barn and paddocks. JBSA work toward arranging for contract to build new barn and paddocks and relocate horses is currently on hold due to Covid-19.
- Salado E. Commerce Trailhead – Under Construction.
- Southside Lions to SE Military – Construction Documents complete. Addressing Development Services Department permitting comments. Anticipate construction start early 2021.
- SE Military to Monte Viejo neighborhood – In Design.

Leon Creek Greenway (Projects listed North to South)

- Leon (Levi Strauss to Lackland Monument site) – Bid opening was held earlier today. Anticipate construction by early 2021.
- Leon (Pearsall to I-35) – Union Pacific Railroad (UPRR) canopy design in design. Land acquisitions and project design will commence when we have UPRR preliminary approval.

Westside Creeks

- Alazan – Under Construction.
- Zarzamora Creek – Under Construction
- Tree Planting Projects
 - Martinez Creek (Cincinnati to Fredericksburg Rd) includes 350 trees – To be completed August 2020.


Tributary Trails, Connections, and Enhancements

- French Creek (Leon Greenway to Nani Falcone Park) – Design Complete. Bid advertisement to be released soon. Anticipate construction start by early 2021.
- Maverick Creek (Huesta Creek Greenway to UTSA Blvd.) and Markson Park – Trail portion is currently under construction. Park design being modified to incorporate additional special needs equipment and facilities.
- Culebra Tributary (Tezel connection) – Design has been completed. Coordinating design and construction plans with Public Works, who is building a community facility at Tezel Road under the 2017 Bond Program. Anticipating construction by early 2021.

Greenway Trails Bicycle and Pedestrian Use*

Estimated average monthly trail use

May through July 2019 compared to May through July 2020

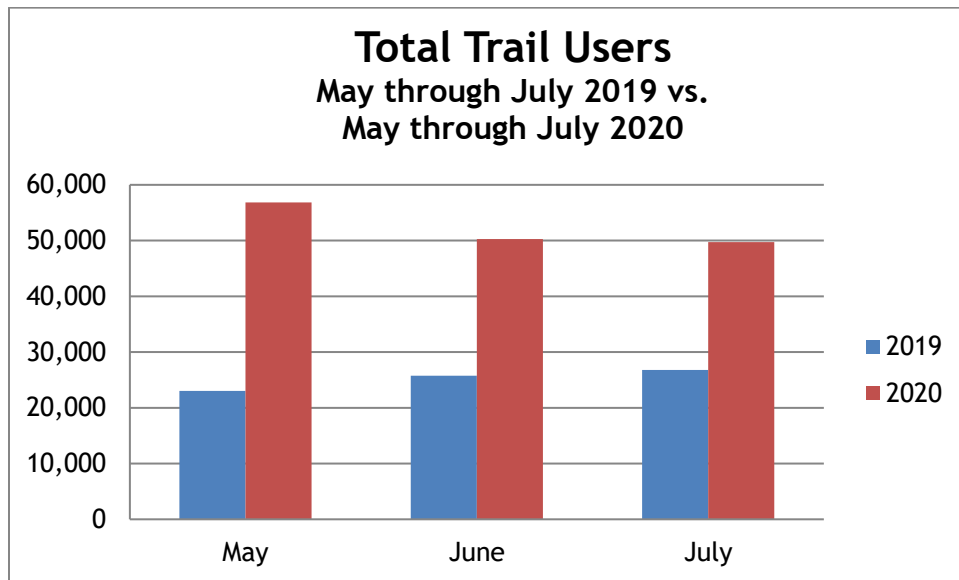

Total Monthly Visitors

2019

May 2019	23,036
June 2019	25,749
July 2019	26,785

2020

May 2020	56,852
June 2020	50,278
July 2020	49,721

Average daily use per counter

2019

May 2019	252
June 2019	282
July 2019	294

2020

May 2020	611
June 2020	542
July 2020	545

*** Trail Counter Locations Include:**

- Leon Greenway near Prue Road
- Leon Greenway near Ingram Road
- Salado Greenway near Blanco Road
